


AM18001 Renovatie en kwaliteitsverbetering rwzi Oijen - planning DO fase met producten



99		056 verwerken opmerkingen	20	4 wkn	maa 30-3-20	din 28-4-20	98
100		057 opstellen kostenraming	10	4 wkn	maa 30-3-20	din 28-4-20	98
101		Werkpakket 06: Nabezinktanks (NT's) incl. retourslibgemaal (RS)	70	dagen	maa 27-1-20	din 5-5-20	
102		061 C	25	dagen	maa 10-2-20	vri 13-3-20	86
103		062 W	0	5 wkn	maa 10-2-20	vri 13-3-20	
104		062 W	40	dagen	maa 27-1-20	vri 20-3-20	90
105		063 E	80	8 wkn	maa 27-1-20	vri 20-3-20	
106		063 E	20	dagen	maa 27-1-20	vri 21-2-20	95
107		tekst	0	4 wkn	maa 27-1-20	vri 21-2-20	
108		schema	0	4 wkn	maa 27-1-20	vri 21-2-20	
109		065 review	0	3 wkn	maa 23-3-20	vri 10-4-20	102;104;106
110		066 verwerken opmerkingen	0	3 wkn	din 14-4-20	din 5-5-20	109
111		067 opstellen kostenraming	0	3 wkn	din 14-4-20	din 5-5-20	109
112		Werkpakket 07: Effluentgemaal (EG)	35	dagen	maa 30-3-20	din 19-5-20	
113		071 C	0	2 wkn	maa 6-4-20	maa 20-4-20	102BE+3 wkn
114		072 W	10	dagen	din 14-4-20	din 28-4-20	104BE+3 wkn
115		tekst (pompen reviseren en afsluiten)	0	2 wkn	din 14-4-20	din 28-4-20	
116		073 E	10	dagen	maa 30-3-20	vri 10-4-20	106BE+5 wkn
117		biotector in gebouw	0	2 wkn	maa 30-3-20	vri 10-4-20	
118		075 review	1	wk	woe 29-4-20	din 5-5-20	113;114;116
119		076 verwerken opmerkingen	0	2 wkn	woe 6-5-20	din 19-5-20	118
120		077 opstellen kostenraming	0	2 wkn	woe 6-5-20	din 19-5-20	118
121		Werkpakket 08: Ingediktlibgemaal (SG) en primairslibgemaal/defosfatering (PG)	80	dagen	vri 10-1-20	maa 4-5-20	
122		081 C	50	55 dagen	vri 10-1-20	don 26-3-20	14
123		uitgangspunten VO uitwerken, wacht op uitslag testen	100	11 wkn	vri 10-1-20	don 26-3-20	
124		082 W	50	11 wkn	vri 10-1-20	don 26-3-20	14
125		083 E	0	11 wkn	vri 24-1-20	don 9-4-20	148E+2 wkn
126		084 BIM	30	11 wkn	vri 10-1-20	don 26-3-20	14
127		085 review	0	1 wk	vri 10-4-20	vri 17-4-20	122;124;125
128		086 verwerken opmerkingen	0	2 wkn	maa 20-4-20	maa 4-5-20	127
129		087 opstellen kostenraming	0	2 wkn	maa 20-4-20	maa 4-5-20	127
130		Werkpakket 09: Slibverwerkingsgebouw	75	dagen	vri 31-1-20	maa 18-5-20	
131		091 C	55	dagen	vri 31-1-20	vri 17-4-20	148E+3 wkn
132		tekst	0	11 wkn	vri 31-1-20	vri 17-4-20	
133		tekeningen (niet in 3D)	0	11 wkn	vri 31-1-20	vri 17-4-20	
134		092 W	50	dagen	vri 31-1-20	don 9-4-20	148E+3 wkn
135		brainstorm afzuiging lucht door piekbelasting laadhal	5	9 wkn	vri 31-1-20	don 2-4-20	
136		tekst	0	10 wkn	vri 31-1-20	don 9-4-20	
137		tekeningen	0	10 wkn	vri 31-1-20	don 9-4-20	
138		093 E	25	dagen	vri 28-2-20	don 2-4-20	
139		E-ruimte verwijderen i.v.m. H2S problemen	0	5 wkn	vri 28-2-20	don 2-4-20	140BE-1 wk
140		094 BIM (opzetten model bestaande situatie)	20	5 wkn	vri 31-1-20	don 5-3-20	148E+3 wkn
141		095 review	0	2 wkn	maa 20-4-20	maa 4-5-20	131;134;138
142		096 verwerken opmerkingen	0	2 wkn	din 5-5-20	maa 18-5-20	141
143		097 opstellen kostenraming	0	2 wkn	din 5-5-20	maa 18-5-20	141
144		Werkpakket 10: Luchtbehandeling	25	dagen	maa 21-10-19	vri 22-11-19	
145		Werkpakket 11: Pacas installatie	105	dagen	vri 10-1-20	don 11-6-20	
146		110 uitgangspunten vaststellen	70	12 wkn	vri 10-1-20	don 2-4-20	14
147		111 C	0	3 wkn	vri 3-4-20	vri 24-4-20	157
148		112 W	0	3 wkn	vri 10-4-20	maa 4-5-20	157BE+1 wk
149		113 E	0	3 wkn	maa 20-4-20	maa 11-5-20	157BE+2 wkn
150		114 technologie	30	3 wkn	vri 3-4-20	vri 24-4-20	157
151		115 review	0	2 wkn	din 12-5-20	woe 27-5-20	158;159;160
152		116 verwerken opmerkingen	0	2 wkn	don 28-5-20	don 11-6-20	162
153		117 opstellen kostenraming	0	2 wkn	don 28-5-20	don 11-6-20	162
154		Werkpakket 12: Terrein	161	dagen	maa 21-10-19	maa 22-6-20	
155		121 C	40	28 wkn	maa 21-10-19	din 19-5-20	
156		update 6 tekeningen	40	28 wkn	maa 21-10-19	din 19-5-20	
157		122 W	0	28 wkn	maa 21-10-19	din 19-5-20	
158		123 E	20	28 wkn	maa 21-10-19	din 19-5-20	
159		124 BIM	40	28 wkn	maa 21-10-19	din 19-5-20	
160		125 review	0	2,2 wkn	woe 20-5-20	maa 8-6-20	166;168;169
161		125a tussentijdse review 1	0	0 uur	don 26-3-20	don 26-3-20	
162		125b tussentijdse review 2	0	0 uur	don 23-4-20	don 23-4-20	
163		126 verwerken opmerkingen	0	2 wkn	din 9-6-20	maa 22-6-20	171
164		127 opstellen kostenraming	0	2 wkn	din 9-6-20	maa 22-6-20	171
165		Werkpakket 13: Bedrijfsgebouw	120	dagen	maa 25-11-19	don 28-5-20	
166		130 uitgangspunten en wensenlijst	80	60 dagen	maa 25-11-19	vri 28-2-20	56
167		131 C / B	30	6 wkn	maa 2-3-20	vri 10-4-20	177
168		132 W	0	6 wkn	maa 9-3-20	maa 20-4-20	177BE+1 wk
169		133 E	0	6 wkn	maa 16-3-20	din 28-4-20	177BE+2 wkn
170		134 BIM	40	6 wkn	maa 2-3-20	vri 10-4-20	177
171		135 review	0	2 wkn	woe 29-4-20	din 12-5-20	178;179;180;
172		136 verwerken opmerkingen	0	2 wkn	woe 13-5-20	don 28-5-20	182
173		137 opstellen kostenraming	0	2 wkn	woe 13-5-20	don 28-5-20	182
174		Werkpakket 14: E-gebouwen	65	dagen	maa 2-3-20	vri 5-6-20	
175		141 gebouw 1 naast bedrijfsgebouw	0	3 wkn	maa 2-3-20	vri 20-3-20	177
176		142 gebouw 2 naast ingedikt slibgemaal	0	3 wkn	maa 16-3-20	vri 3-4-20	186BE-1 wk
177		143 gebouw 3 naast fys. voorzuivering	0	3 wkn	din 21-4-20	din 12-5-20	47;48;49;50
178		144 BIM	0	6 wkn	maa 30-3-20	din 12-5-20	181BE-2 wkn
179		145 review	0	1 wk	woe 13-5-20	din 19-5-20	186;187;188;
180		146 verwerken opmerkingen	0	1 wk	woe 20-5-20	don 28-5-20	190
181		147 opstellen kostenraming	0	2 wkn	woe 20-5-20	vri 5-6-20	190
182		Werkpakket 15: Proces Automatisering	35	dagen	woe 20-5-20	vri 10-7-20	
183		151 procesautomatisering overall	10	4 wkn	woe 20-5-20	vri 19-6-20	190
184		152 review	0	1 wk	maa 22-6-20	vri 26-6-20	194
185		153 verwerken opmerkingen	0	2 wkn	maa 29-6-20	vri 10-7-20	195
186		154 opstellen kostenraming	0	1 wk	maa 22-6-20	vri 26-6-20	194
187		Werkpakket 16: Chemicaliëndosering (Al)	1	dag?	maa 21-10-19	maa 21-10-19	
188		161	80	4 dagen	maa 16-3-20	don 19-3-20	103
189		162 review	0	1 wk	vri 20-3-20	don 26-3-20	199
190		163 verwerken opmerkingen	0	1 wk	vri 27-3-20	don 2-4-20	200
191		164 opstellen kostenraming	0	1 wk	vri 3-4-20	don 9-4-20	201
192			0	dagen	maa 21-10-19	maa 21-10-19	
193		Bestuurlijke planning besluitvorming uitvoeringscrediet	34	dagen	maa 24-8-20	vri 9-10-20	
194		PHO (24 augustus 2020)	0	dagen	maa 24-8-20	maa 24-8-20	24
195		DB (1 september 2020)	0	dagen	din 1-9-20	din 1-9-20	
196		commissie EB (17 september 2020)	0	dagen	don 17-9-20	don 17-9-20	
197		AB (9 oktober 2020)	0	dagen	vri 9-10-20	vri 9-10-20	
198		Uitvoeringskrediet definitief	0	dagen	vri 9-10-20	vri 9-10-20	208

21-10

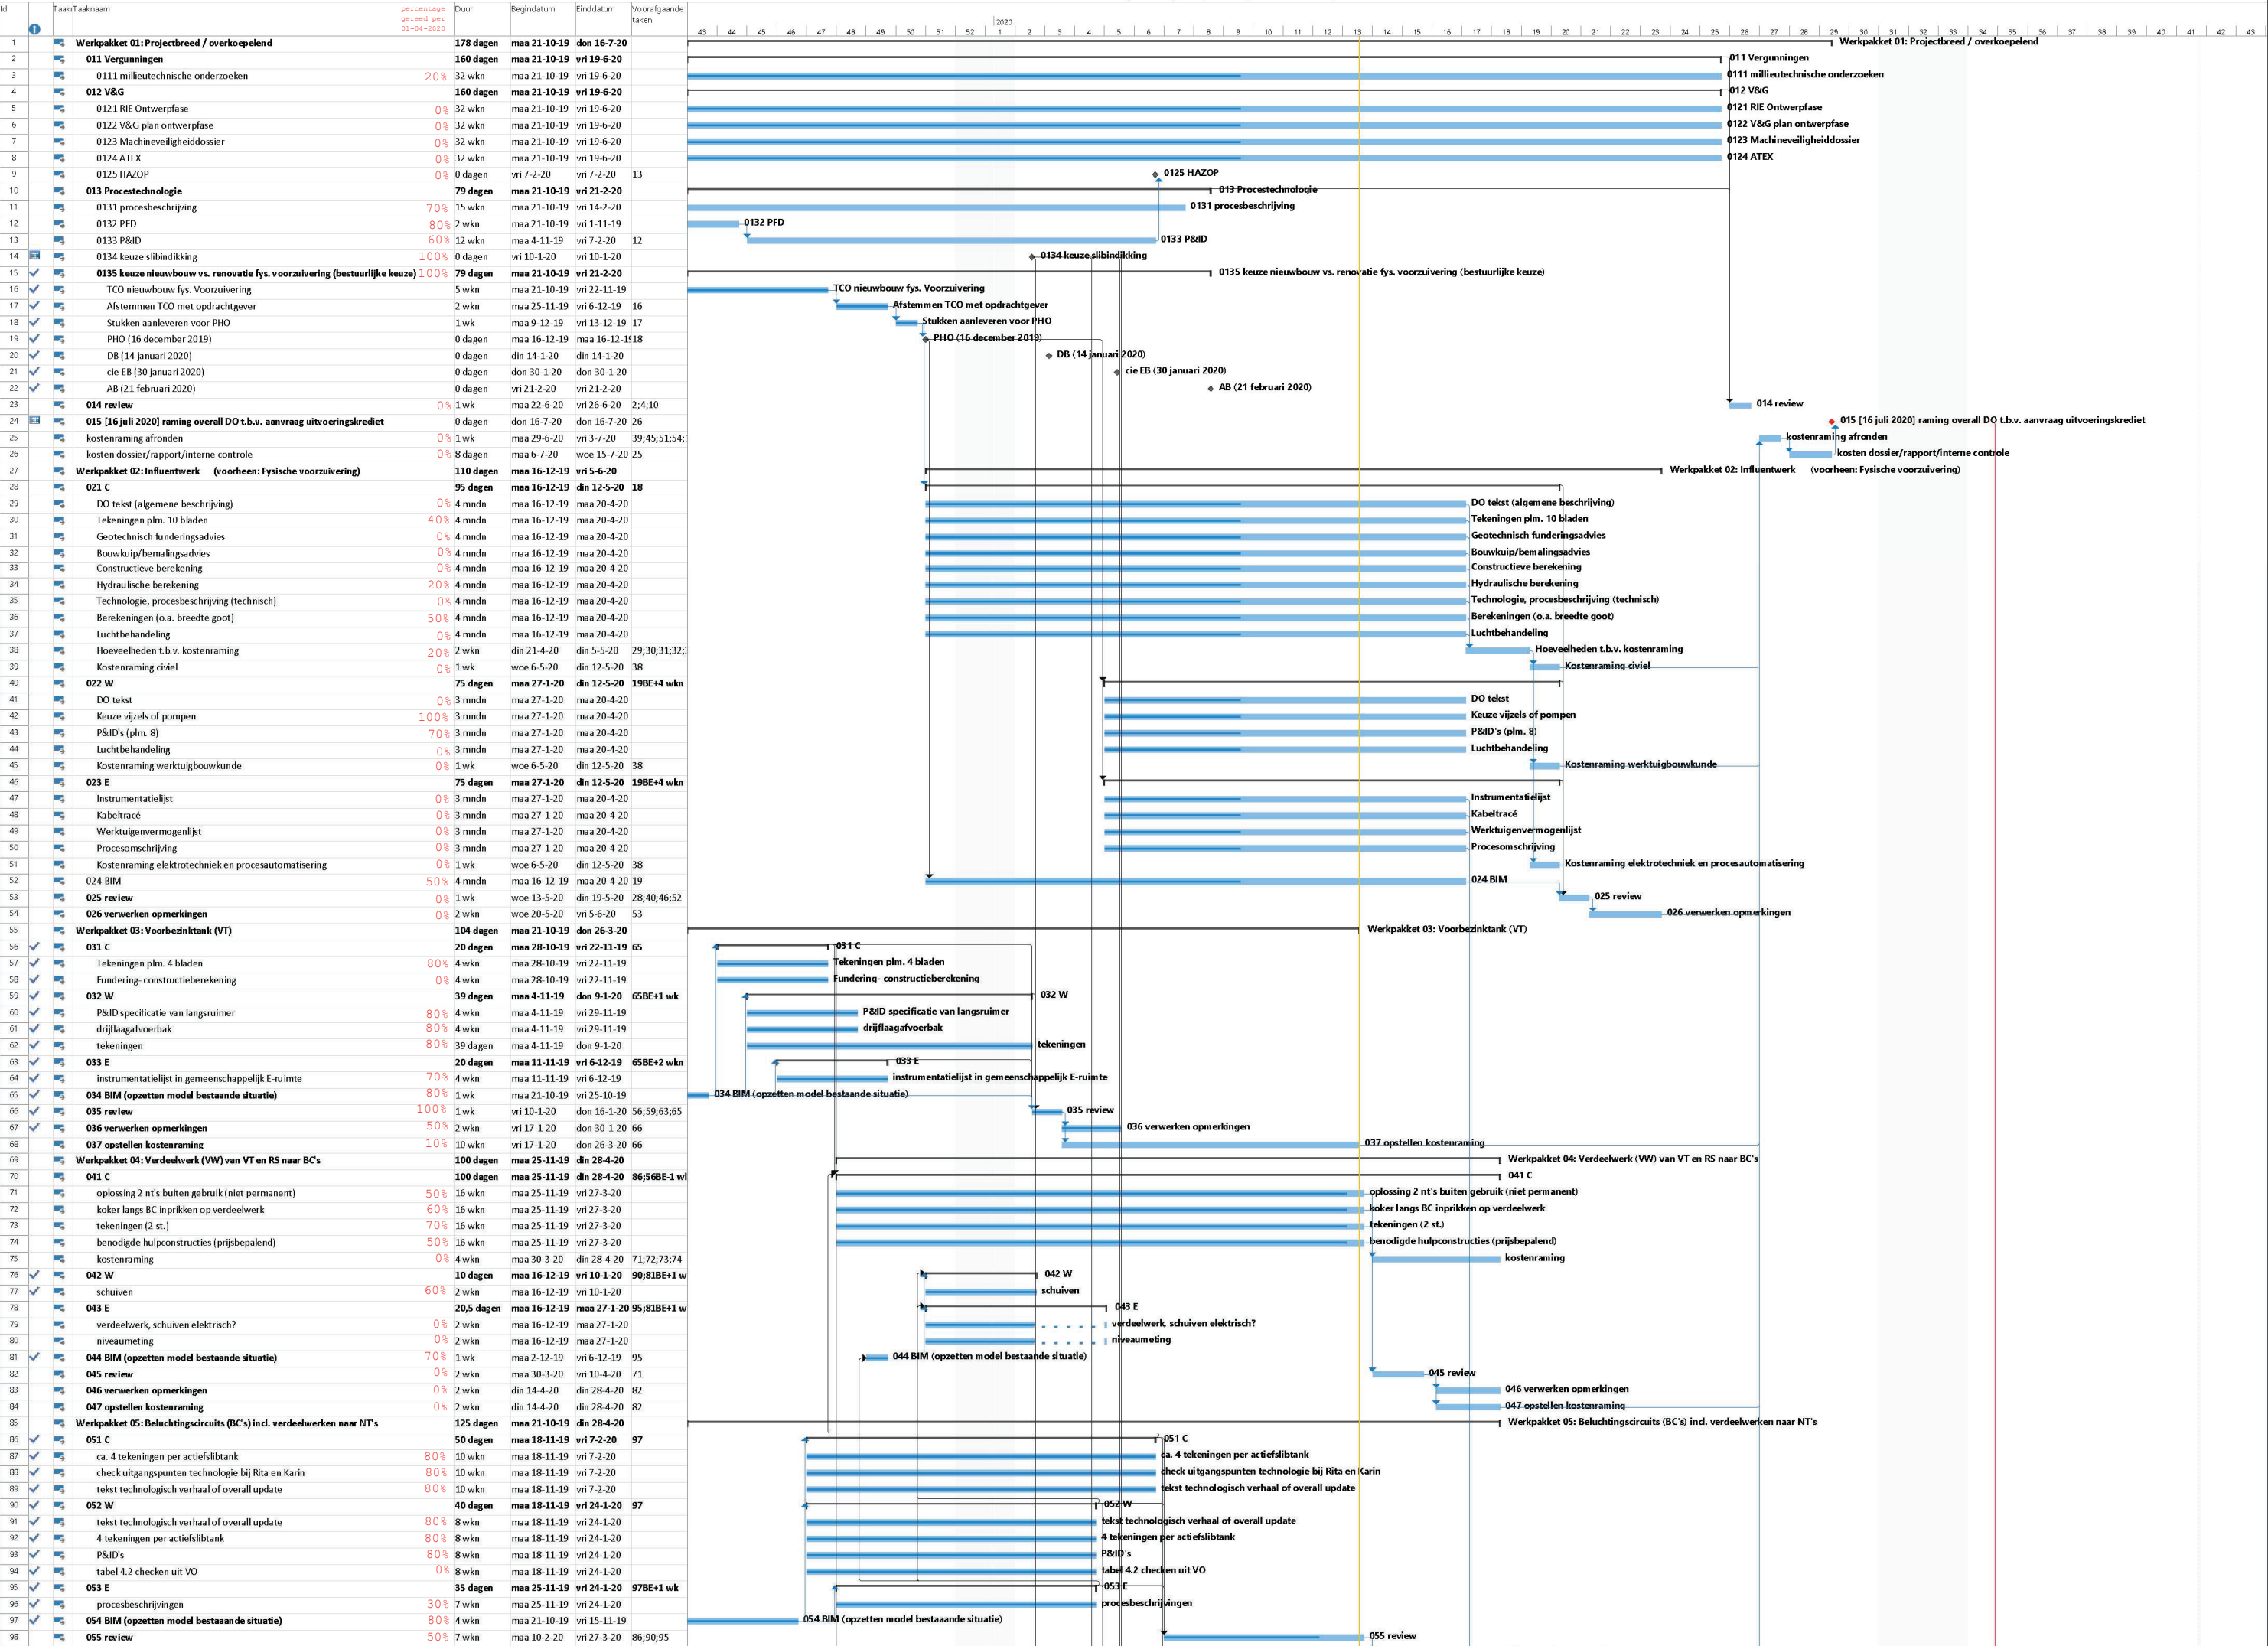
